Rotary
Club of Nairobi Lang'ata

RCL SERVICE PROJECT
DIGITAL LITERACY PROGRAM (DLP)



Nairobi, Kenya
District 9212
(Kenya, Ethiopia, Eritrea, South Sudan)

Compiled by;
Quinter Peres-Service Project Director
Email: serviceprojects@rotaryclubofnairobilangata.org

Rotary Year: 2025/26

Fun in Service

UNITE FOR GOOD



Table of Contents

Table of content..... 2
RCL Board of Directors..... 3
RCL Committee chairs..... 3
Introduction..... 4
Avenue of Service..... 4
Rotary Area of Focus..... 4
Mission statement..... 4
Service Project Committee members..... 5
Service Project Committee Advisory Team..... 5
Digital Literacy Program (DLP)..... 6
DLP Background..... 7
DLP Problem statement..... 7
Digital Literacy solution..... 7
Components of a DLP Lab..... 7
DLP Implementations Steps & Procedures..... 8
DLP Monitoring and Evaluation..... 8
DLP Evaluation Tools & Methodologies..... 8
DLP M & E Schedule..... 8
DLP Project Sustainability..... 8
DLP Project Implementation Work Plan..... 9
DLP Contribution to SDG's..... 9
DLP Implementation/Procurement Matrix..... 10
Completed DLP Projects..... 11
Ongoing DLP Implementation projects..... 14
DLP Implementation progress in Kenya..... 15
Proposed Schools in the Pipeline..... 16
Project Budget for the next 5 schools..... 17
RCL overal Project Budget..... 18
RCL Service Project Bank Account details..... 19
DLP Photo gallery..... 20
Refference..... 21
Past President of RCL..... 22

BOARD OF DIRECTORS 2025/2026



Erick Sangoro
President



Maina Njonjo
President Elect & Club Admin Chair



Serah Wanjau
IPP & Club Trainer



Sam Alosa
Vice President & Membership Director



Anne-Simone Nyeretse
Club Secretary & Data Protection Officer



Kevin Ng'eno
Treasurer




Sharon Olbara
Assistant Treasurer



John Nyagah
Sergent at Arms



Quiner Peres
Service Projects Director



David Kariuki
Family of Rotary



Susan Chege
Vocational Service Director



Charlene Migwi
Rotary Foundation Director




Paul Mbugua
PR & Comms Director

COMMITTEE CHAIRS 2025/2026




Vivian Perose
Governance & Ethics Chair



Joe Waweru
My Rotary Chair



Erick Otieno
Attendance Officer



Tony Githua
Youth Service Chair



Sarah Njau
Speaker Secretary



Winnie Gor
Sunshine Rally Chair



Maureen Gichuhi
Grants Chair



Cinju Muiruri
Fundraising Chair



Dr. Moka Lantum
International Service Chair



Oscar Njuguna
RI Convention Chair



Sam Kamunya
DCA Chair



Rosana Munyiva
Monitoring & Evaluation Chair

Introduction

Rotary is a global network of more than 1.2 million neighbors, friends, leaders, and problem-solvers who see a world where people unite and take action to create lasting change across the globe, in our communities, and in ourselves. Solving real problems takes real commitment and vision. For more than 110 years, Rotary's people of action have used their passion, energy, and intelligence to take action on sustainable projects. From literacy and peace to water and health, we are always working to better our world, and we stay committed to the end.

The Rotary Club of Nairobi-Lang'ata (RCL) was chartered on 14th May 2002 and has 149 members as of July 2025 making it one of the biggest Clubs in District 9212. RCL have 75+ Paul Harris Fellows and our members are servicing both at Rotary International and District level. Our dynamic club has also sponsored more than 2 Rotary Clubs, 2 Rotaract Clubs and 1 Interact Club.Our club theme is Unlimited Fun in Service, which was borne out of making our membership experience not only fun, but also worthwhile as Rotarians.

Avenue of Service

The Avenues of Service are the philosophical and practical framework that RCL operates under. This includes;

1. Club Service,
2. Youth Service,
3. Vocational Service,
4. Community Service,
5. International Service.

Rotary Area Of Focus

The work of Rotary begins in the community, and every community has its own unique needs and concerns. While the RCL serves in countless ways, the Club's efforts shall be focused in seven key areas to maximize impact. These areas as recognized by Rotary International encompass some of the world's most critical and widespread humanitarian needs, and Rotary worldwide has a proven record of success in addressing them. This includes;



Our mission: We provide service to others, promote integrity, and advance world understanding, goodwill, and peace through our fellowship of business, professional, and community leaders.

Vision statement: Together, we see a world where people unite and take action to create lasting change — across the globe, in our communities, and in ourselves.

RY 2025/26 Service Project Goals

1. Basic Education & Literacy: 5 DLP's, 4 Books donation.
2. Environment Protection: 3
3. WASH: 4
4. Economic and Community Development: 3
5. Disease Prevention and Treatment: 1
6. Caravan: 3 & 2 Mini-Caravan
7. Telling our Stories: Highlighting our impact

Service Project Committee (RY:2025/26)

The Rotary Club of Nairobi Langata executes its mandate through committees. This Committees are responsible for implementing the Club's annual and long-term objectives in alignment with the five Avenues of Service. Specifically, the Service Projects Committee is tasked with developing and executing initiatives that support and guide Club members in fulfilling their community engagement responsibilities. This committee oversees all community service activities undertaken by the Club, ensuring they are effectively planned and carried out in accordance with the Rotary Area of Focus, Club's mission and goals. For this Rotary Year, the following are the committee members;



Quinter Peres
Committee Lead



Jeff Gitau
WASH Lead



Billy Okendo
School Lighting Lead



Mahlet Kiflu
Committee PR Lead



PP Edge Mugo
Technical Lead



Angelica Waweru
Disease P & T Lead



Michael Kingori
Environment Lead



Faith Gathungu
Peace& Conflict Lead



PP Beryl Ouma
Maternal & Child Health Lead



Dimitri Macridis
Economic & Community Development Lead



Emmanuel Miyanga
DLP Lead



Edith Kwamboka
Committee Support Lead

Service Project Committee Advisory Team



Sam Alosa



Carol Mburu



IPP Serah Njoroge



Githinji Nderitu

DIGITAL LITERACY PROGRAM(DLP)

BASIC EDUCATION AND LITERACY



A ROTARY CLUB OF NAIROBI LANGATA FLAGSHIP PROJECT PIONEERED BY PAST PRESIDENT KIZITO MAKATIANI

Digital Literacy Program (DLP)

DLP Background: Increasingly, all aspects of life are moving online. Through smartphones and computers, we are trading, working, collaborating, learning, interacting digitally more than at any other time in human history. The Covid-19 pandemic accelerated the global movement towards digitisation. However, digital growth is not taking place evenly.

DLP Problem statement: Many young people in rural communities and in vulnerable, underserved areas of Africa are being left behind in the drive towards digitisation. This is due to the high cost of internet access, the lack of consistent electricity supply and a lack of infrastructure that would support digital learning.

In 2016, the government of Kenya initiated the Digital Literacy Programme, providing locally-made tablets and laptops to students in public schools to facilitate digital learning. The government also provided solar solutions for schools that were not connected to the national electricity grid and funding for digital literacy programmes in private schools. In practice, however, not every school in Kenya has equal access to this state funding. Where this is the case, parents of students often cannot afford to fund the construction and maintenance of computer labs in schools. Even where computers are available, little progress is made as teachers often do not have the training to use digital tools. Further, there is insufficient maintenance of the computers.

As a result, many students are growing up unprepared for the digital future that awaits them.

Digital Literacy solution



Infrastructure

Build and maintain model computer labs (Computers, Internet Maintenance & Security)



Content

Enriched learning resources and content



Capacity

Digital skills training, capacity building for teachers

OUR Ambitious goal is to bring digital access and literacy to over 5,000 students and 100 teachers in primary schools in underserved communities across Kenya between 2021-2026

This effort will:


- Enhance learning in primary schools
- Students acquire technical skills and efficiency as they learn to use devices, software and online platforms as well as equipping them with knowledge about online safety, privacy, and security
- Set young people on the path to becoming global digital citizens, able to compete for jobs and to build and lead the digital businesses of the future, at par with their global peers.

Components of a DLP Lab

- **Physical Infrastructure** - The classroom will be reinforced to secure the learning equipment by burglar proofing, Alarm system, CCTV.
- **Furniture** -This include worktops, chairs, computer cages
- **Electrical & Data Cabling**
- **Computer hardware** - 25 computers (24 Student / 1 Teacher), 1 printer and 1 projector, Inverter and UPS

- **Computer software** - Microsoft operating system, office software, Kenya Institute of Curriculum Development (KICD) approved learning content, other relevant Edutech.
- **Teacher Training** – At least 5 teachers per school will be trained on computer literacy and content delivery to the learners as well as integrating the ICT into the school curriculum.
- **Monitoring & Evaluation** – Continuous M&E will be provided to ensure objectives of the projects are met and gaps addressed as we move along
- **Maintenance** – There will be quarterly preventive hardware maintenance and continuous resolution of issues raised by teachers.
- **Mentorship** – To be provided by Rotary Club members to pupils, teachers and parents.

DLP Implementations Steps & Procedures

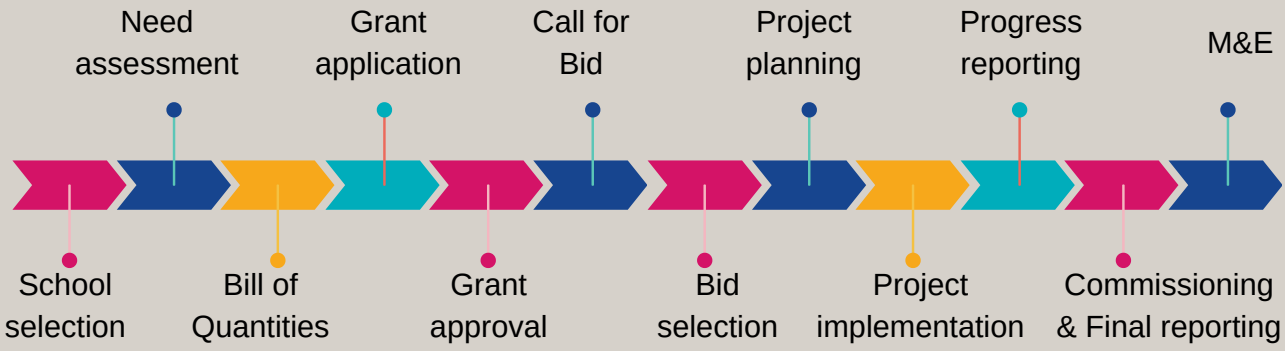

DLP Monitoring and Evaluation

- Supervise timely and complete implementation of the project deliverables,
- Adequately capture lessons learned during each school's DLP implementation and carry these forward to subsequent schools' projects,
- Assess DLP's impact over the next 3 years,
- Enhance DLP's transparency and accountability,

DLP Evaluation Tools & Methodologies

- Monitoring and evaluation framework, Student and teacher surveys & Analysis of students' performance over time

DLP M & E Schedule:

Baseline Survey: At project Initiation	Short Term (After 3 months) of implementation.	Mid Term After 1 year of implementation.	Long Term: After 2 years of implementation.

DLP Project Sustainability

DLP project sustainability is driven by Rotary of Nairobi-Langata (RCL) through regular M&E, Computer for Schools- Kenya (CFSK); and The Beneficiary School Community this includes; Teachers, Students, PTA, Parents & Alumni Association. This is achieved by the following measures; Training of the Teachers to be involved in the digital literacy program in the school, CFSK provides annual support and maintenance for the hardware and resolve any issues arising, Partnering with the Alumni members who have an interest in the school to continue supporting and supervising the project, Creating awareness to the parents and the community on the importance of the digital literacy project, Training the pupils on the proper handling and utilization of the gadgets provided to ensure their life is prolonged, Student champions to support the teachers during the lessons, Ensuring security of the computer lab is always enhanced and scheduled Project monitoring & evaluation.

DLP Project Implementation Work Plan

Project Activity	Purpose	Timeline
Baseline survey & Documentation	Validate existing physical infrastructure, Identify the needs of the school and appropriate approach for effective implementation.	2 Days
Sensitization	Creating awareness among Board of Management, teachers, students, parents, and the host community on the importance of this project.	1 Day
Development of training resources	In line with Computers for Schools Kenya ICT curriculum, training content and digital platform.	5 Days
Infrastructure Setup		
Inspection of computer labs	To ascertain that they meet the required standards for teaching & learning, security of the equipment &setup	1 Day
Site Analysis for the Local Area Network.	To identify the type of network that is most suitable To identify the quantities of each network material required according to the size of the room	1 Day
Setting up of the Local Area Network	To ensure the setup of a fresh network connectivity in the computer lab	2 Days
Software installation and testing of computers	To ensure that all the equipment set for deployment are in good working conditions, with requisite software's	1 Day
Deployment of equipment to the school	For transportation and installation of equipment at the approved institutions	1 Day
Training of Teachers		
Orientation of instructors	For demonstration of the training resources.	2 Days
Training of teachers	To equip trainees with necessary skills for digital content development and capacity development.	5 Days
Monitoring, Evaluation and Reporting		
Monitoring and evaluation	To track and measure project progress against set objectives	Project Life
Reporting	To confirm the activities undertaken, show impact of the project and way forward	Monthly Reports

DLP Initiative contributes to the UN Sustainable Development Goals (SDGs)



Relevant technical skills and access to education content



Promoting digital access to male and female students



Increasing job prospects and reducing the likelihood of unemployment




Driving access to information and communications technology



Avenue of strengthening the means of global partnership

DLP Project Implementation/Procurement Matrix

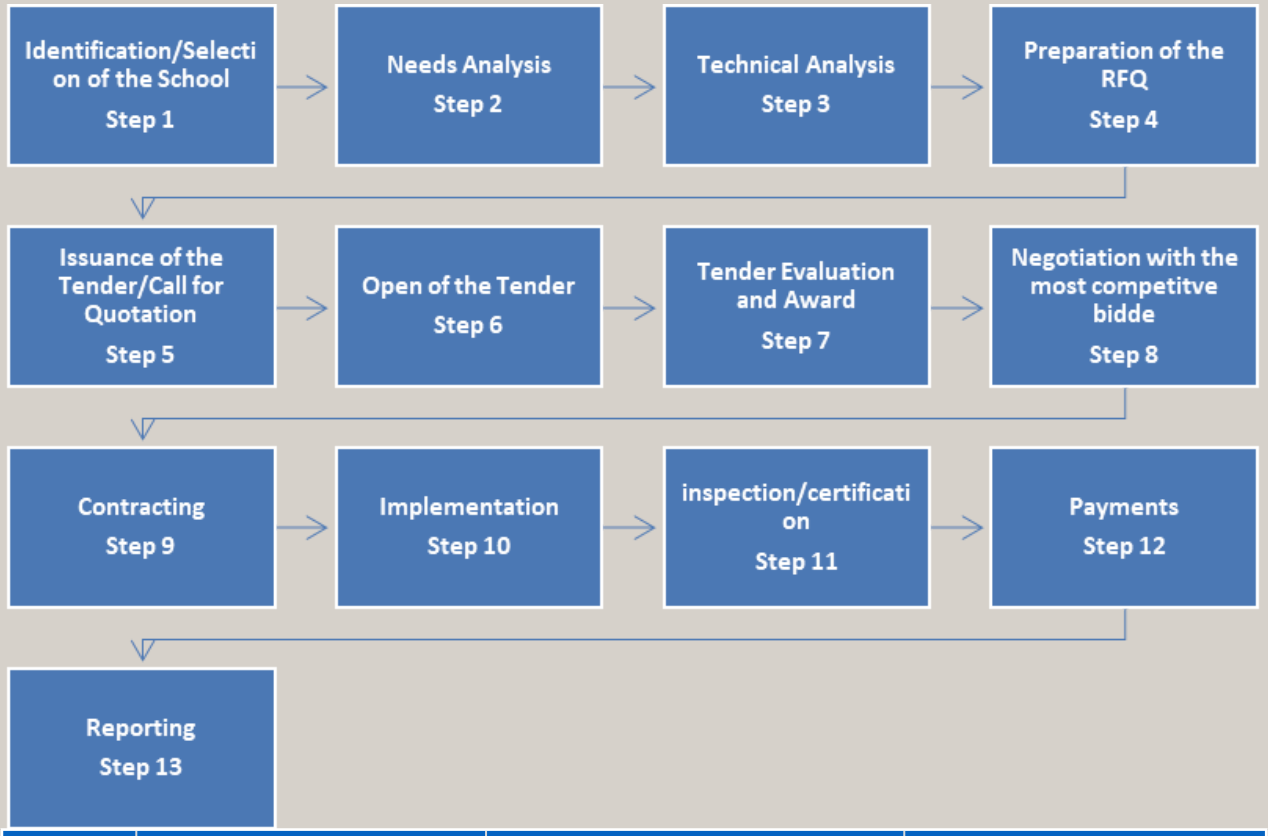

STEPS	PROCESS	RESPONSIBLE	TIME FRAME
1	Identification/Selection of the School	RCL Members & DLP Committee	30 days after the call for nomination
2	Needs Analysis	Project Lead/Project Sponsor	1 day
3	Technical Analysis	Director Projects	2 days
4	Preparation of the RFQ	Procurement	7 days
5	Issuance of the Tender/ Call for Quotation	Procurement	14 days
6	Open of the Tenders	Procurement	1 day
7	Pre-Qualification /Award	Procurement	1 day
8	Negotiation with the Lowest Bidder	Procurement	1 day
9	Contracting	Procurement	5 days
10	Implementation	Project Lead/Sponsor	30 days
11	inspection/certification	Director Project & Project Lead/Sponsor	2 days
12	Payments	PL/PS/DP/CT	2 Days
13	Reporting	Project Lead/Sponsor	30 days

Completed DLP Projects

1. Kingeero Primary School-Kiambu

Project HandedOver:7-5-2022
Total Cost: US$28,600
Partners:
RC Brampton (Canada)
RC North Point
All Trusted Medical
TBM
Measurable Outcomes:

- **Teachers Trained:** 10
- **Children Reached:** 498

Media Link: (Click here)





2. Kamburaini Primary School Lab - Nyeri

Project Handed Over: 2nd July 2022
Total Cost: US$27,900
Partners: Vitol Foundation
Measurable Outcomes:

- **Exam Avg:**
  2021(Before DLP): 229.95
  2022: 228.45
  2023: 234.34
  2024: TBA 2025
- **Teachers Trained: 5**
- Children Reached: 333
  Media Link: (Click here)





3. Kibaoni Primary School Lab - Lamu

Project Handed Over: 26th November 2022
Total Cost: US$27,900 (TRF Grant No:GG2234219)
Partners:
RC Brampton (Canada)
RC Suntec-City (Singapore)
RC Malindi (Kenya)
Imarika Foundation (Kenya)
Serianu Limited (Kenya)
Measurable Outcomes:
Teachers Trained: 10
Children Reached: 1034

Media Link: (Click here)





4. Tenderfoot School Lab - Kiambu

Project Handed Over: 10th February 2024
Total Cost: US$21,600 (TRF Grant No:GG2238525)
Partners:
RC Cataraqui-Kingston (Canada)
RC Medicine-Hat (Canada)
RC Nipigon (Canada)
RC Madras-Coromandel (India)
DDF (Districts 7040, 5580,7430,9212)
Measurable Outcomes:

- **Exam Avg:**
  2023(Before DLP): 311
  2024: TBA 2025
- **Teachers Trained:** 10
- **Children Reached:** 90

Media Link: (Click here)





5. Tigoni Primary School Lab - Kiambu

Project Handed Over: 16th March 2024
Total Cost: US$21,600 (TRF Grant No:GG2238525)
Partners:
RC Cataraqui-Kingston (Canada)
RC Medicine-Hat (Canada)
RC Nipigon (Canada)
RC Madras-Coromandel (India)
DDF (Districts 7040, 5580,7430,9212)
Measurable Outcomes:

- **Teachers Trained: 10**
- **Children Reached:** 1353

Media Link: (Click here)





6. Watamu Primary School Lab

Project Handed Over: 25th April 2024
Total Cost: US$30,000 (DDF Grant No: DG2460561)
Partners:
DDF (Districts 9212) – US$ 22,000
Measurable Outcomes:

- **Teachers Trained: 5**
- **Children Reached:** 986

Media Link: (Click here)





7. Shisasari Primary School Lab - Kakamega

Project Handed Over: 22nd July 2023
otal Cost: US$27,900 (TRF Grant No:GG2234219)
Partners:
RC Brampton (Canada)
RC Suntec-City (Singapore)
RC Malindi (Kenya)
Imarika Foundation (Kenya)
Serianu Limited (Kenya)

Measurable Outcomes:

- **Teachers Trained:** 10
- **Children Reached: 600**
  Media Link: (Click here)





8. Nairobi South Primary School- Nairobi

Project Handed Over:30th Aug 2025
Total Cost: US$21,600 (TRF Grant No:GG2238525)
Partners:
RC Cataraqui-Kingston (Canada)
RC Medicine-Hat (Canada)
RC Nipigon (Canada)
RC Madras-Coromandel (India)
DDF (Districts 7040, 5580,7430,9212)
Measurable Outcomes:

- **Teachers Trained: 10**
- **Children Reached:** 1353

Media Link: (Click here)









Ongoing DLP Implementation projects

2 Kiawaroga Primary School – Kiambu

Is an ordinary public educational institute in Karambaini, Limuru, Kenya.
This school is managed / sponsored by central government/deb and has three systems of education Early Childhood Development (ECD) running from PP 1 to PP2, Competence Based Curriculum (CBC) system from Grade 1 to 6 and Junior Secondary Grade 7 and 8-4-4 system -Standard 8 (last class in 844 System). Projected handover date is 20th September 2025

Student Population: 755 Students (Boys 407 / Girls 348)
Average Number of Students Per Class: 48 / 2 Streams Per Class
Main Economic Activity of the Parents: Work in Tea Plantations and Subsistent farming to feed the family and sell the surplus at the local markets

Sustainability of the Project:

- School Community: BOM, PTA, Teachers and Parents
- Active Alumni Association
  Who have indicated their willingness to meet all recurring Costs










DLP Implementation progress across the country

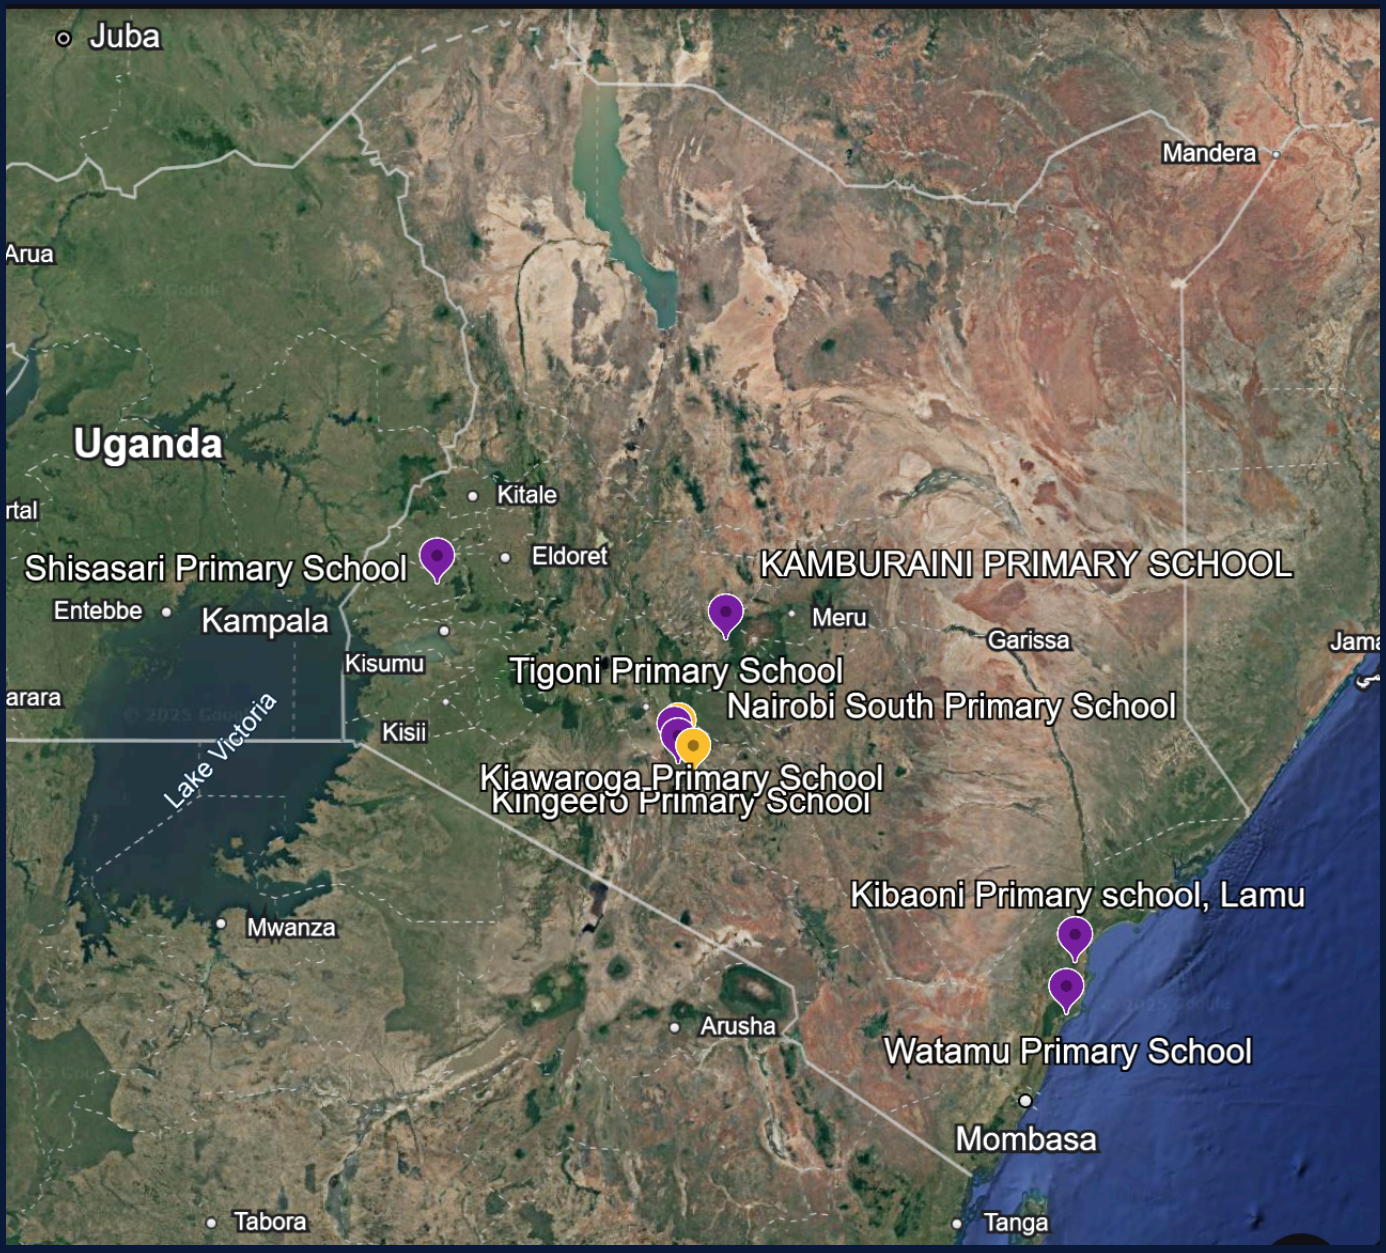

Completed Projects **Implementation ongoing**

Proposed Schools in the Pipeline

1. Mwarano Primary School-Muranga
2. Ralak Girls Secondary School-Siaya
3. Matu Primary School- Muranga
4. Kholera Primary School- Mumias
5. Kimutwa Primary School- Machakos
6. Gitare Primary School, Kiambu
7. Gachie Primary School-Kiambu
8. Kinyanjui Road School
9. Daho Primary School-Siaya
10. Kimoning Primary School – Uasin Gishu
11. Moody Awori Primary School - Busia
12. Murubara primary and JS school
13. Siranga Primary School- Siaya
14. Baitígítú primary school- Meru
15. Vidhu Ramji Primary School
16. Kaliini Primary School
17. Mbeletu Primary School

RCL DLP Projects per County

COUNTY	IMPLEMENTATION
1. Mombasa County	0
2. Kwale County	0
3. Kilifi County	1
4. Tana River County	0
5. Lamu County	1
6. Taita/Taveta County	0
7. Garissa County	0
8. Wajir County	0
9. Mandera County	0
10. Marsabit County	0
11. Isiolo County	0
12. Meru County	0
13. Tharaka-Nithi County	0
14. Embu County	0
15. Kitui County	0
16. Machakos County	0
17. Makueni County	0
18. Nyandarua County	0
19. Nyeri County	1
20. Kirinyaga County	0
21. Murang'a County	0
22. Kiambu County	3
23. Turkana County	0
24. West Pokot County	0
25. Samburu County	0
26. Trans Nzoia County	0
27. Uasin Gishu County	0
28. Elgeyo/Marakwet County	0
29. Nandi County	0
30. Baringo County	0
31. Laikipia County	0
32. Nakuru County	0
33. Narok County	0
34. Kajiado County	0
35. Kericho County	0
36. Bomet County	0
37. Kakamega County	1
38. Vihiga County	0
39. Bungoma County	0
40. Busia County	0
41. Siaya County	0
42. Kisumu County	0
43. Homa Bay County	0
44. Migori County	0
45. Kisii County	0
46. Nyamira County	0
47. Nairobi City County	2

Project Itemised Budget for the next 5 schools

GLOBAL GRANT 3 - INDICATIVE BUDGET COSTS		Total Cost for Five (5) Schools
Type	**Budget Detail**	**USD**
	Refurbishment	
Refurbishment	Class Room Refurbishment / Painting	34,925.00
	Furniture	
Furniture	13 Double Student Work Stations	16,760.00
Furniture	26 Pupils Computer Chair	1,575.00
Furniture	1 Teachers Desk	727.00
Furniture	1 Teachers Chair	161.00
Furniture	Printer Desk	606.00
Furniture	Whiteboard,duster rail and Notice Boards	727.00
Furniture	Projector cage	121.00
	ICT	
Cabling	Structured / Electrical / Data Cabling	12,840.00
IT Hardware	CCTV Cameras	2,742.00
IT Hardware	Alarm System	3,308.00
IT Hardware	Access Control System	2,621.00
IT Hardware	UPS	13,859.00
IT Hardware	Projector/Projector Mount & Screen	5,371.00
IT Hardware	Wireless Printer	1,736.00
IT Hardware	Internet Connectivity	808.00
IT Hardware	25 Computers	26,351.00
IT Software	Digital Learning Content	7,027.00
IT Software	Classroom Management Software	1,757.00
Operations	Teacher Training	2,342.00
Publicity	Project Branding	3,231.00
Publicity	Media / Photography /Videography	4,038.00
Operations	Project Management	5,250.00
M&E	Monitoring and Evaluation	4,806.00
Operations	Student Dignity Packages	1,413.00
	Subtotal	**155,102.00**
Operations	Contingency 10% of Total Cost	15,513.00
	TOTAL BUDGETED COST	**170,615.00**

RCL OVERAL SERVICE PROJECT BUDGET RY:2025/26

DLP Projects		
Name of Project	**Total Cost in KES**	**Total Cost in USD**
Kiawaroga Primary School, Kiambu (Ongoing)	Ksh3,415,000.00	$28,458.33
Nairobi South Primary School, NBO (Ongoing)	Ksh3,165,000.00	$26,375.00
DLP Mwarano Primary School	Ksh4,715,000.00	$39,291.67
Kholera Primary School- Mumias	Ksh4,715,000.00	$39,291.67
Kimutwa Primary School- Machakos	Ksh4,715,000.00	$39,291.67
Modern ICT lab - Busia	Ksh4,715,000.00	$39,291.67
Gitare Primary School , Kiambu	Ksh4,411,666.67	$36,763.89
Kimoning Primary School – Uasin Gishu	Ksh3,482,166.67	$29,018.06
Ralak Girls Secondary School- Siaya	Ksh4,715,000.00	$39,291.67
Matu Primary School- Muranga	Ksh4,715,000.00	$39,291.67

Wash Projects		
Name of Project	**Total Cost in KES**	**Total Cost in USD**
Uranga Primary School	Ksh785,000.00	$6,541.67
Gakoigo Primary School Wash project	Ksh1,384,180.00	$11,534.83
Nyabera Primary school	Ksh835,000.00	$6,958.33
Kiamiciri Primary School	Ksh1,767,000.00	$14,725.00

Environment Conservation Projects		
Name of Project	**Total Cost in KES**	**Total Cost in USD**
Tree Planting	Ksh765,000.00	$5,884.62
Planting 100 trees in 50 schools in Matungu Constituency	Ksh285,000.00	$2,192.31
Ngong hills Wash & Bin	Ksh518,720.00	$3,990.15

Community Development		
Name of Project	**Total Cost in KES**	**Total Cost in USD**
Lighting Project	Ksh3,260,000.00	$24,149.00
Nyabera Primary school Class room	Ksh1,050,000.00	$8,750.00

TOTAL BUDGET:$432,192.21

ROTARY CLUB OF LANGATA SERVICE PROJECT BANKACCOUNT DETAILS

CURRENCY : KES
ACCOUNT NAME: ROTARY CLUB OF LANGATA SERVICE PROJ (KES)
BANK ADDRESS : P.O . BOX 30550-00100, NAIROBI - KENYA
BANK NAME: STANBIC BANK KENYA LIMITED
BANK BRANCH : INTERNATIONAL HOUSE
ACCOUNT NUMBER : 0100014750902
SWIFT CODE : SBICKENX

CURRENCY : USD
ACCOUNT NAME: ROTARY CLUB OF LANGATA SERVICE PROJ (USD)
BANK ADDRESS : P.O . BOX 30550-00100, NAIROBI - KENYA
BANK NAME: STANBIC BANK KENYA LIMITED
BANK BRANCH : INTERNATIONAL HOUSE
ACCOUNT NUMBER : 0100009937492
SWIFT CODE : SBICKENX

DLP Photo Gallery












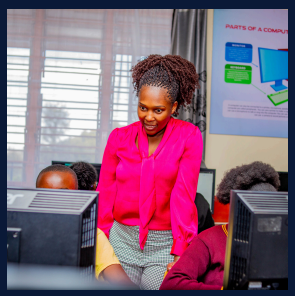

















10. Reference:

1. https://my.rotary.org/
2. RCL By-laws 2024/25
3. https://sdgs.un.org/goals
4. https://ict.go.ke/digital-literacy-programmedlp
5. https://thedocs.worldbank.org/en/doc/967221540488971590-0050022018/original/KennedyOgolaEntryDigitalLiteracyKenya.pdf

Presidents Of Rotary Club Of Nairobi Langata



Alex Nyaga
2001-2003



Antoinette Absaloms
2003-2004



Beryl Ouma
2004-2005



Muchau Githiaka
2005-2006



Mutula Kilonzo Junior
2006-2007



Peter S. Kariuki
2007-2008



Edward Mugo
2008-2009




Nicholas Bore
2009-2010



George Masese
2010-2011



Maina Gichohi
2011-2012



Irene Wamakau
2012-2013



Bashir Mburu
2013-2014



Sailepu Montet
2014-2015



Janet Onyango
2015-2016



June Rienye
2016-2017



Ashley Myers
2017-2018




Nahashon Omondi
2018-2019



Michael Kimani
2019-2020



Sarah Migwi
2020-2021



Kizito Makatiani
2021-2022



Abdi Dubat
2022-2023



Muchai Mathare
2023-2024



Serah Njoroge
2024-2025



President Eric Sangoro
2025-2026

Rotary
Club of Nairobi Lang'ata



Fun in Service

Contact details
Email: serviceprojects@rotarycluboflangata.org
cc: rotarylangata@gmail.com

UNITE FOR GOOD
